Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish
Submittals					
1000	Notice to Proceed	0	0	28JAN19 *	
1000	GC submittals	30d	30d	28JAN19	08MAR19
1010	Plumbing submittals	30d	30d	28JAN19	08MAR19
1020	HVAC submittals	30d	30d	28JAN19	08MAR19
1030	Electrical submittals	30d	30d	28JAN19	08MAR19
1040	Glass & Glazing submittals	30d	30d	28JAN19	08MAR19
1110	GC material delivery	50d	50d	18FEB19	26APR19
1120	HVAC material delivery	50d	50d	11MAR19	17MAY19
1130	Electrical material delivery	50d	50d	11MAR19	17MAY19
1140	Glass & glazing material delivery	50d	50d	11MAR19	17MAY19
1280	Summer 2019 break	0	0	24JUN19 *	
1370	Summer 2020 break	0	0	22JUN20 *	
Elementary School					
1050	Demo + reconstruct main offices	80d	80d	28JAN19	17MAY19
1060	Demo + reconstruct Art	80d	80d	28JAN19	17MAY19
1090	Construct telecom rooms	15d	15d	28JAN19	15FEB19
1070	Main office addition	80d	80d	01APR19	22JUL19
1100	Classroom renovations - first group of 4	30d	30d	20MAY19	28JUN19
1350	Window replacements	75d	75d	20MAY19	02SEP19
1180	Asbestos abatement	10d	10d	24JUN19	08JUL19
1200	Replace switchgear	10d	10d	24JUN19	08JUL19
1210	Replace lighting and ceilings in corridors	50d	50d	24JUN19	02SEP19
1150	Classroom renovations - second group of 4	30d	30d	01JUL19	12AUG19
1190	Band/orchestra renovations	20d	20d	09JUL19	05AUG19
1160	Classroom renovations - third group of 4	30d	30d	13AUG19	23SEP19
1170	Classroom renovations - fourth group of 4	30d	30d	24SEP19	04NOV19
1260	Classroom renovations - fifth group of 4	30d	30d	05NOV19	16DEC19
1270	Classroom renovations - sixth group of 4	30d	30d	17DEC19	28JAN20
1280	Classroom renovations - seventh group of 4	30d	30d	30JAN20	11MAR20
1290	Classroom renovations - eighth group of 4	30d	30d	12MAR20	22APR20
1420	Gym floor replacement	40d	40d	22JUN20	14AUG20
Middle / High School					
1250	Construct telecom rooms	30d	30d	28JAN19	08MAR19
1400	Tech area renovations	35d	35d	20MAY19	08JUL19
1230	Asbestos abatement	25d	25d	24JUN19	29JUL19
1410	FACS renovations	40d	40d	24JUN19	19AUG19
1240	Demo + reconstruct HS main offices	80d	80d	30JUL19	18NOV19
1220	Demo + reconstruct MS main offices	80d	80d	20AUG19	09DEC19
1360	Window replacements	75d	75d	03SEP19	16DEC19
1300	Classroom renovations - first group of 4	30d	30d	10DEC19	22JAN20
1310	Classroom renovations - second group of 4	30d	30d	23JAN20	04MAR20
1320	Classroom renovations - third group of 4	30d	30d	05MAR20	15APR20
1330	Classroom renovations - fourth group of 4	30d	30d	16APR20	27MAY20
1340	Classroom renovations - fifth group of 4	20d	20d	28MAY20	24JUN20
1380	Replace lighting and ceilings in corridors	50d	50d	22JUN20	28AUG20
1390	HVAC + Electrical work in mechanical room	45d	45d	22JUN20	21AUG20
Sitework					
1430	Tennis Court and Athletic Field work	45d	45d	24JUN19	26AUG19
1440	Reconstruction of Elm Street Parking lot and	50d	50d	22JUN20	28AUG20

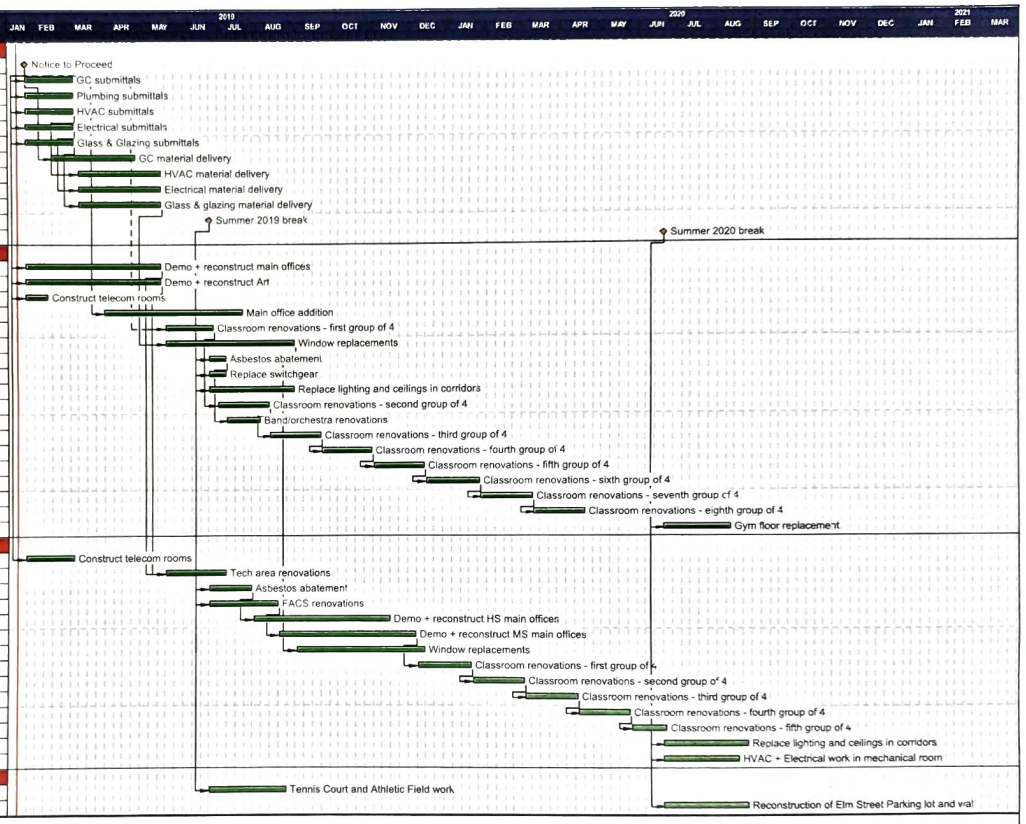

Start date	21JAN19
Finish date	28AUG20
Data date	21JAN19
Run date	15NOV18
Page number	1A

© Primavera Systems, Inc.

HR Beebe, Inc
Clinton CSD Phasing

HRBeebe
